


Scope Creep:

Recognising and Addressing Scope Creep in Consulting Engagements

Scope creep is a common challenge in the consulting world, where project goals and deliverables can evolve or expand beyond the initial agreed-upon scope. Unchecked scope creep can lead to budget overruns, missed deadlines, and strained client relationships. As a consultant, it is crucial to proactively recognise and address scope creep, establish clear definitions and boundaries, and develop strategies for managing scope changes and additional requests.

Recognising Scope Creep

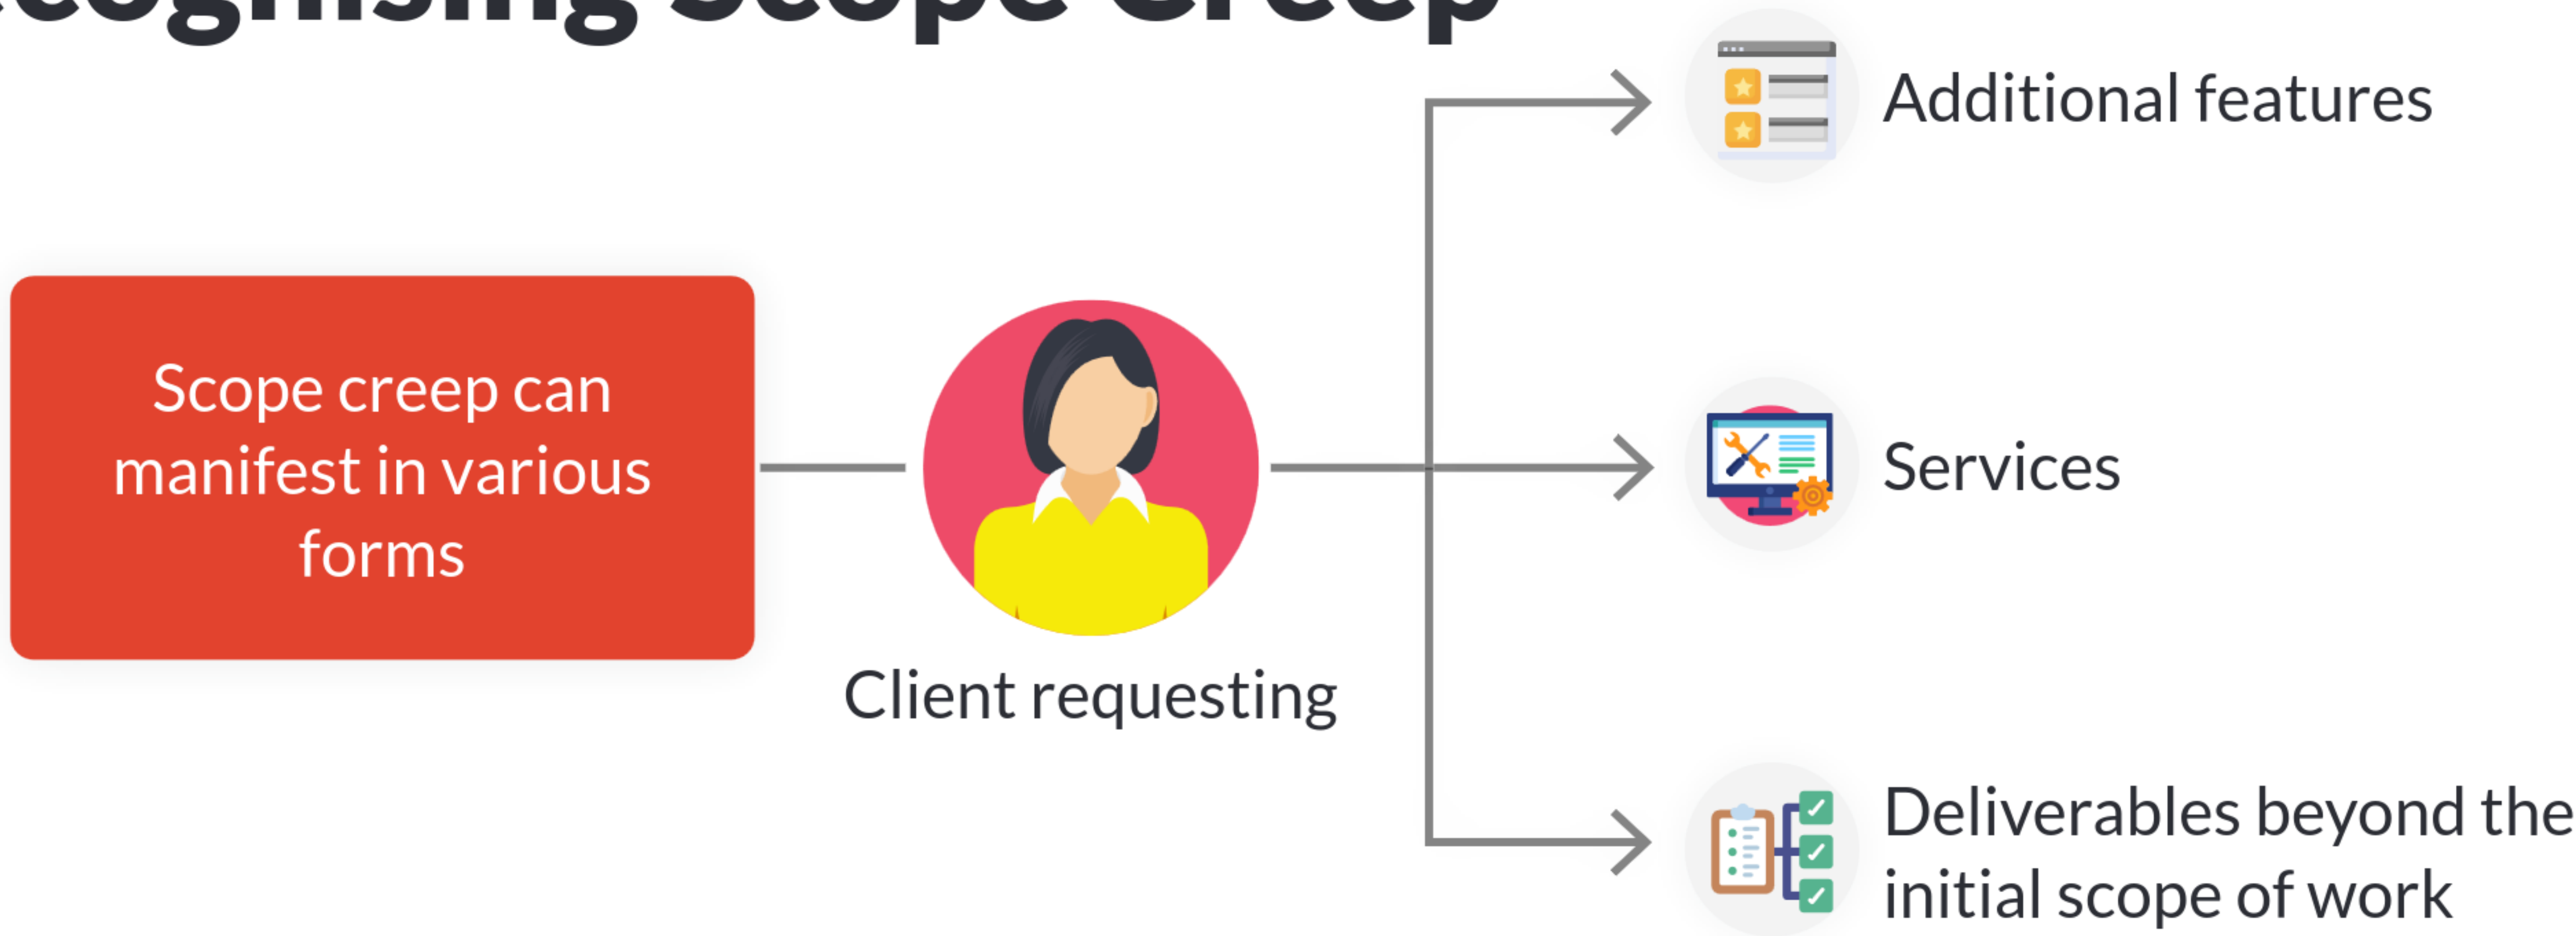

It can also occur when project requirements or goals shift midway through an engagement or when stakeholders introduce new priorities or objectives.

To recognise scope creep, it is essential to have a clear and documented understanding of the initial project scope, deliverables, and timelines. Regularly review project progress against these baselines and be vigilant for deviations or requests outside the agreed-upon scope.

Establishing Clear Scope Definitions and Boundaries

Preventing scope creep starts with establishing clear scope definitions and boundaries from the outset of the engagement. Work closely with the client during the scoping and contracting phase to define the project’s goals, deliverables, timelines, and success criteria.

Create a detailed scope of work document outlining the tasks, milestones, and responsibilities for the consulting team and the client. Delineate what is included and excluded from the scope and establish a process for addressing potential changes or additions.

SIMPLE SCOPE OF WORK TEMPLATE

PROJECT NAME	Electric Vehicle-Charging Station Installations
COMPANY NAME	Positive Charge
POINT OF CONTACT	Wendy Williams
PHONE	765-876-9876
EMAIL	Wendy.Williams@positivecharge.com
COMPANY MAILING ADDRESS	9016 NE 184th Boswell, WA 98011
PROJECT LOCATION	[various] U.S., Mexico, Canada
AUTHOR	Jane Matthews
DATE	XX/XX/XX

SCOPE OF WORK
What does the project entail? What are the delivery methods?
Installation of 1,125 EV charging stations at 116 locations across the US, Mexico, and Canada to accommodate multi- and service stations' EV-charging needs. Full details of the scope of this work are included in the attached documents, but, broadly, this project will entail the following for 17 unique sites in 3 different countries, and will include: Site Analysis; Infrastructural Planning; Utility Assessment; Integration; Final Prep; and Installation.
PROJECT DELIVERABLES
Note the tangible products / services resulting from this project.
Installations of 1,125 fully functional and licensed EV charging stations at 116 locations across the US, Mexico, and Canada - 1,000 EV charging station in s. California - 100 in Canada - 25 in Mexico (see attached spec for geo-specific locations).
